

86 Lytton Street Lot 1 DPS 1595 Section _____ Block _____

ROTORUA CITY COUNCIL


(Connection to Common Sewer)

(Appn No: ~~4698~~)

Owner: J. Hoskins

Plumber:

Drainlayer: Goodrick & Alding Ltd



Valuation No.: 651/523/1

Permit No.: 6218

Appn No.: 4698

INSPECTIONS

Date

3-9-75

Damage Tested (Existing drains renewed.)

Entered on Master File & Plan.





4698

CITY OF ROTORUA

Valuation No. 651/523/1.

APPLICATION FOR PERMIT TO CARRY OUT SANITARY PLUMBING AND DRAINAGE WORK

I, the undersigned, hereby apply for permission to have the work described herein and set out on the plans attached hereto, carried out in accordance with the provisions of the Drainage and Plumbing Regulations 1959 at premises situated at:

Address 86 Lytton St

Legal Description:

Lot No. 12 Deposited Plan No. 1595

Section No. _____ Block No. _____

Description of Work: connection to common sewer
off drive in 11 Sophia St.

Name and address of Person for whom work is to be carried out:

Mr Hosking 86 Lytton St.

Name and address of Registered Plumber: _____

Name and address of Registered Drainlayer: _____

GOODRICK & ALDING LTD.
P.O. BOX 680,
ROTORUA

	VALUE	FEES
Plumbing	\$:	\$:
Drainage	\$ 186 :	\$ 3 :00
TOTAL FEES		\$ 3 : -

Signature: P.D. [Signature]

Date: 2/9/75.

FOR OFFICE USE ONLY

Date Received _____

Fee Paid \$3.00 RS17343

Date Paid 2/9/75

Issue Approved [Signature]

Date Approved 2-9-75.

Permit No. 6218

Date Issued 2-9-75

See reverse for Fees and Notes.

FOR OFFICE USE ONLY

FEE PAYABLE ON THE ISSUE OF ANY PLUMBING OR DRAINAGE PERMIT

according to the Estimated Value of Work

Value of work (including value of fittings)

Dollars	Dollars
up to 100	1.50
101 - 200	3.00
201 - 400	6.00
401 - 600	8.00
601 - 800	10.00
801 - 1000	12.00
1001 - 1200	14.00
1201 - 1400	16.00
1401 - 1600	18.00
1601 - 1800	20.00
1801 - 2000	22.00

2001 and over, 1 dollar extra for every \$200 or part thereof in excess of 2000 dollars.

IMPORTANT

INSPECTION & TESTING REQUIREMENTS

Drainage Work: Drainlayers are required to notify the Plumbing and Drainage Inspector when all work is completed. This includes effluent disposal systems for septic tanks. All drains will be tested with a 5ft head of water. To implement this test it will be necessary for persons undertaking drainage work to have sufficient drain plugs to fill all sections of the drain prior to the Plumbing and Drainage Inspector arriving on the job, also to have available a stand pipe to apply the 5ft head pressure.

This form of testing is essential to exclude the possibility of ground water infiltration with its attendant increase in pumping charges and overloading of the sewers and treatment plant.

Plumbing Work: Plumbers are required to notify the Plumbing and Drainage Inspector when work is ready for inspection as follows:

- (a) When the building has been initially piped out and wastes are installed (before wall linings are fixed and floors laid).
- (b) When work is complete.

Plans of Drainage and Plumbing work:

In the case of single houses a preliminary drainage plan will not be required. In all other cases, however, plans of the preliminary proposal are to be submitted at the time of application for a permit. In all instances, however, an "as laid" plan must be available on site as a prerequisite to a test of the work.

In commercial buildings full plans and elevations of plumbing stacks must be provided at the time of application for a permit.

Plans MUST show figured dimensions
and distances from section boundaries


Rotorua City Council

DRAINAGE PLAN

SCALE: IN. TO A FOOT

NEW SEWERAGE DRAINS—RED
STORMWATER—DOTTED BLACK
OLD DRAINS—FULL BLACK

651/523/1

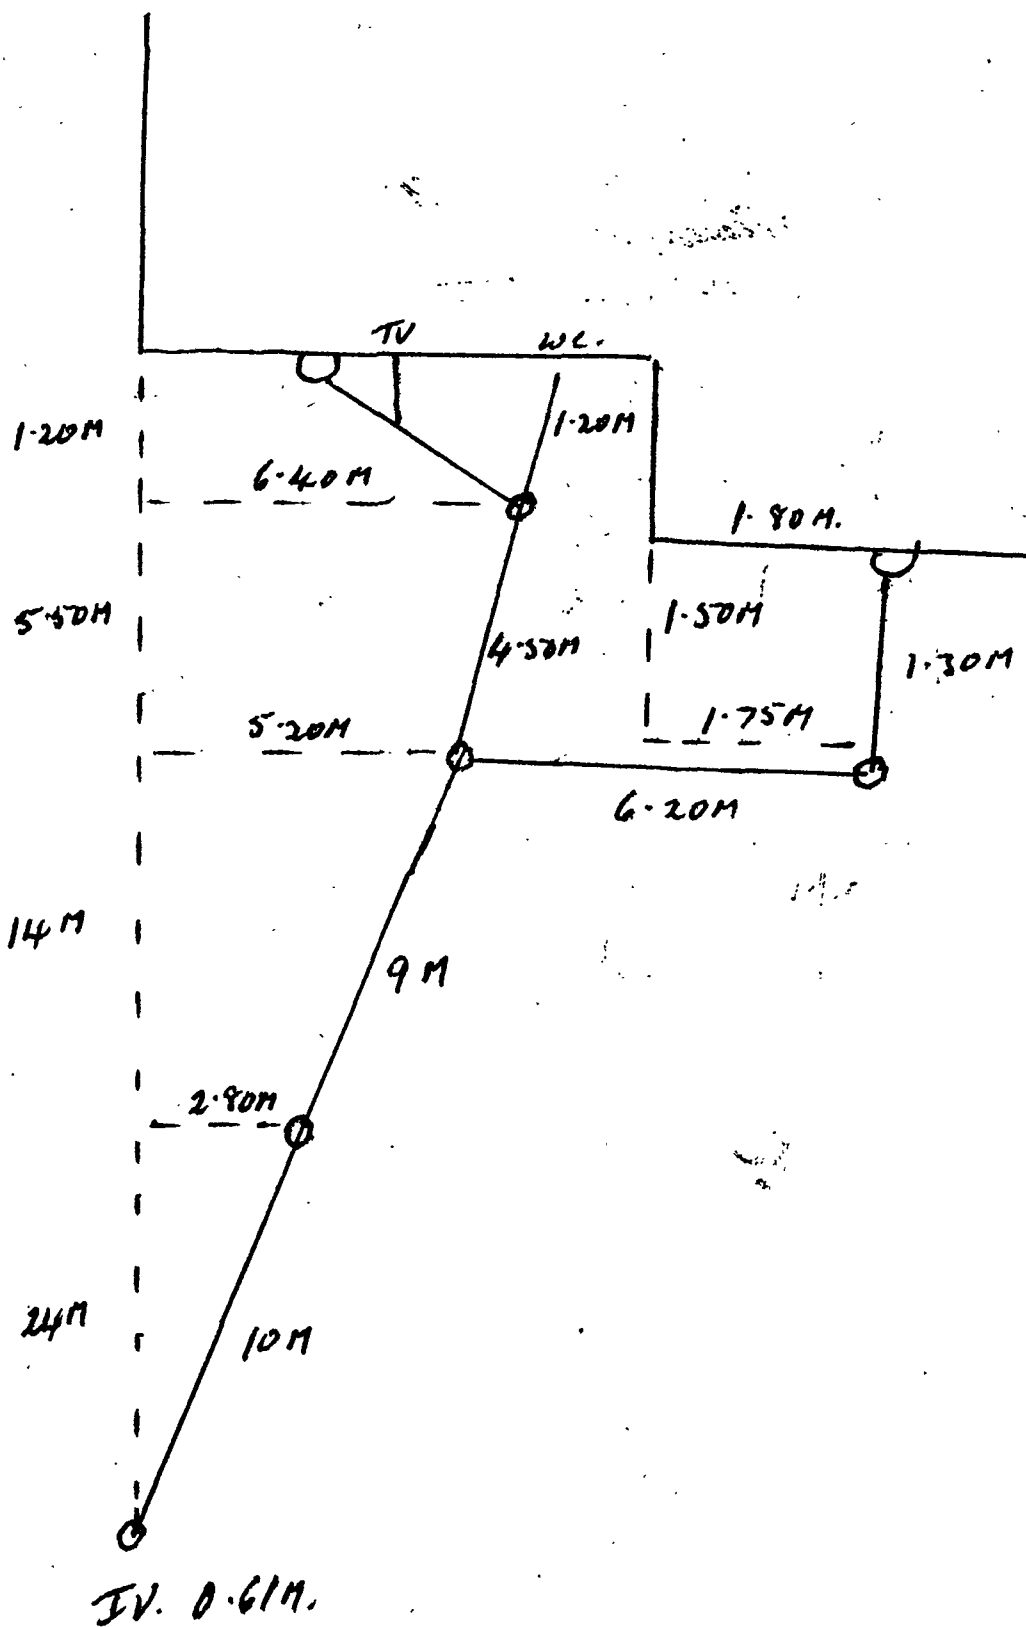

OWNER

Mr. H. King

LOT

1

DP 1595

SEC.

BL.

No.

STREET

St. Lytton

SIGNATURE

OF DRAINLAYER

A. J. King

DATE

3/9/75

MUST show figured dimensions
distances from section boundaries

Rotorua City Council DRAINAGE PLAN

NEW SEWERAGE DRAINS—RED
STORMWATER—DOTTED BLACK
OLD DRAINS—FULL BLACK

SCALE: IN. TO A FOOT

